Data Date :31-Aug-18 Run Date : 19-Oct-18
TASK filter: Submittal Schedule_1.

Royal Inland Hospital Patient Care Tower Project - Project Schedule

Date	Revision	Checked	Approved
19-Oct-18	Financial Close Schedule		

Activity ID	Activity Name	Original Duration	Start	Finish
Royal Inland Hospital Patient Care Tower Project - Project Schedule		671	03-Jul-18 A	31-May-21
Design Process Sch 2 Sec 5.3 and App 2C Sec 4		634	20-Aug-18 A	07-Apr-21
Schematic Design Phase (Early Works)		71	05-Sep-18	14-Dec-18
SD-200	Draft Pkg Delivered to IH	1	05-Sep-18*	05-Sep-18
SD-210	Wait Time between Submission and UCGs	7	06-Sep-18	12-Sep-18
SD-220	Clinical : User Consultation Meeting	2	03-Oct-18*	04-Oct-18
SD-230	Technical : User Consultation Meeting	0	04-Oct-18	04-Oct-18
SD-240	Project to Circulate Live Minutes	2	05-Oct-18	09-Oct-18
SD-250	Informal Feedback from the Authority	2	05-Oct-18	09-Oct-18
SD-252	Arch background Freeze for SD Formal Submission	23	10-Oct-18	09-Nov-18
SD-254	MEIT Co-ordination & Production for SD Formal Submission	20	19-Oct-18	16-Nov-18
SD-256	QA/QC Review and Print	5	19-Nov-18	23-Nov-18
SD-260	Project Co., Prepare & Submit for Formal Schematic Design Submittal	0		23-Nov-18
SD-270	Authority Review Timeline for Formal Schematic Design	15	26-Nov-18	14-Dec-18
Early Works_Utility Relocates[Water,Gas,Sewer,Propane,RTU1,TMP,Exiting,Demo,Hydro,Tree Removal,Piles		26	05-Sep-18	11-Oct-18
EW-100	Project Co., submit draft early works submittal component list and agenda to Authority	1	05-Sep-18*	05-Sep-18
EW-110	Submit Draft Site Utility Relocation Early works Submittal to Authority	1	12-Sep-18	12-Sep-18
EW-120	project Co., to present material to Authority	1	02-Oct-18	02-Oct-18
EW-130	Authority Reviews Early Works Submittal Material	1	03-Oct-18	03-Oct-18
EW-140	Authority Provides Feedback to Project Co.,	0		03-Oct-18
EW-150	Project Co., Submits Final Early works Site Utility Relocation Submittal	1	04-Oct-18	04-Oct-18
EW-160	Authority Review Timeline for Final Early Works Site Utility Relocation Submittal	4	05-Oct-18	11-Oct-18
Design Development Phase		161	20-Nov-18	18-Jul-19
DD#1		43	20-Nov-18	28-Jan-19
DD-100	Consultant Co-Ordination and Production for DD # 1 QA/QC Review	19	20-Nov-18	14-Dec-18
DD-110	ED Receives DD#1 Pkg for QA/QC (Including MEP Info)	0		14-Dec-18
DD-120	QA/QC Review by ED/Trades/FM & QA/QC Mark up issued for Consultant	2	17-Dec-18	18-Dec-18
DD-130	Consultant prepare Revised Pkg & Issue to ED	2	19-Dec-18	20-Dec-18
DD-140	ED/Trades/FM QA/QC # 2	1	21-Dec-18	21-Dec-18
DD-145	Consultant prepare Revised Pkg & Issue to ED	4	27-Dec-18	02-Jan-19
DD-150	Issue to Printer	0		02-Jan-19
DD-160	Print Dwg	2	03-Jan-19	04-Jan-19
DD-170	Draft Pkg Delivered to IH DD#1	1	07-Jan-19	07-Jan-19
DD-210	Wait Time between Submission and UCGs	7	07-Jan-19	13-Jan-19
DD-220	Clinical : User Consultation Meeting	5	14-Jan-19	18-Jan-19
DD-230	Technical : User Consultation Meeting	3	21-Jan-19	23-Jan-19
DD-240	Project to Circulate Live Minutes	8	17-Jan-19	28-Jan-19
DD-250	Informal Feedback from the Authority	8	17-Jan-19	28-Jan-19
Authority Issuance of 100% Specs for Equipment		0	28-Jan-19	28-Jan-19
A3460	Authority to Issue 100% Specs for Equipment	0		TBD
DD#2		53	24-Jan-19	09-Apr-19

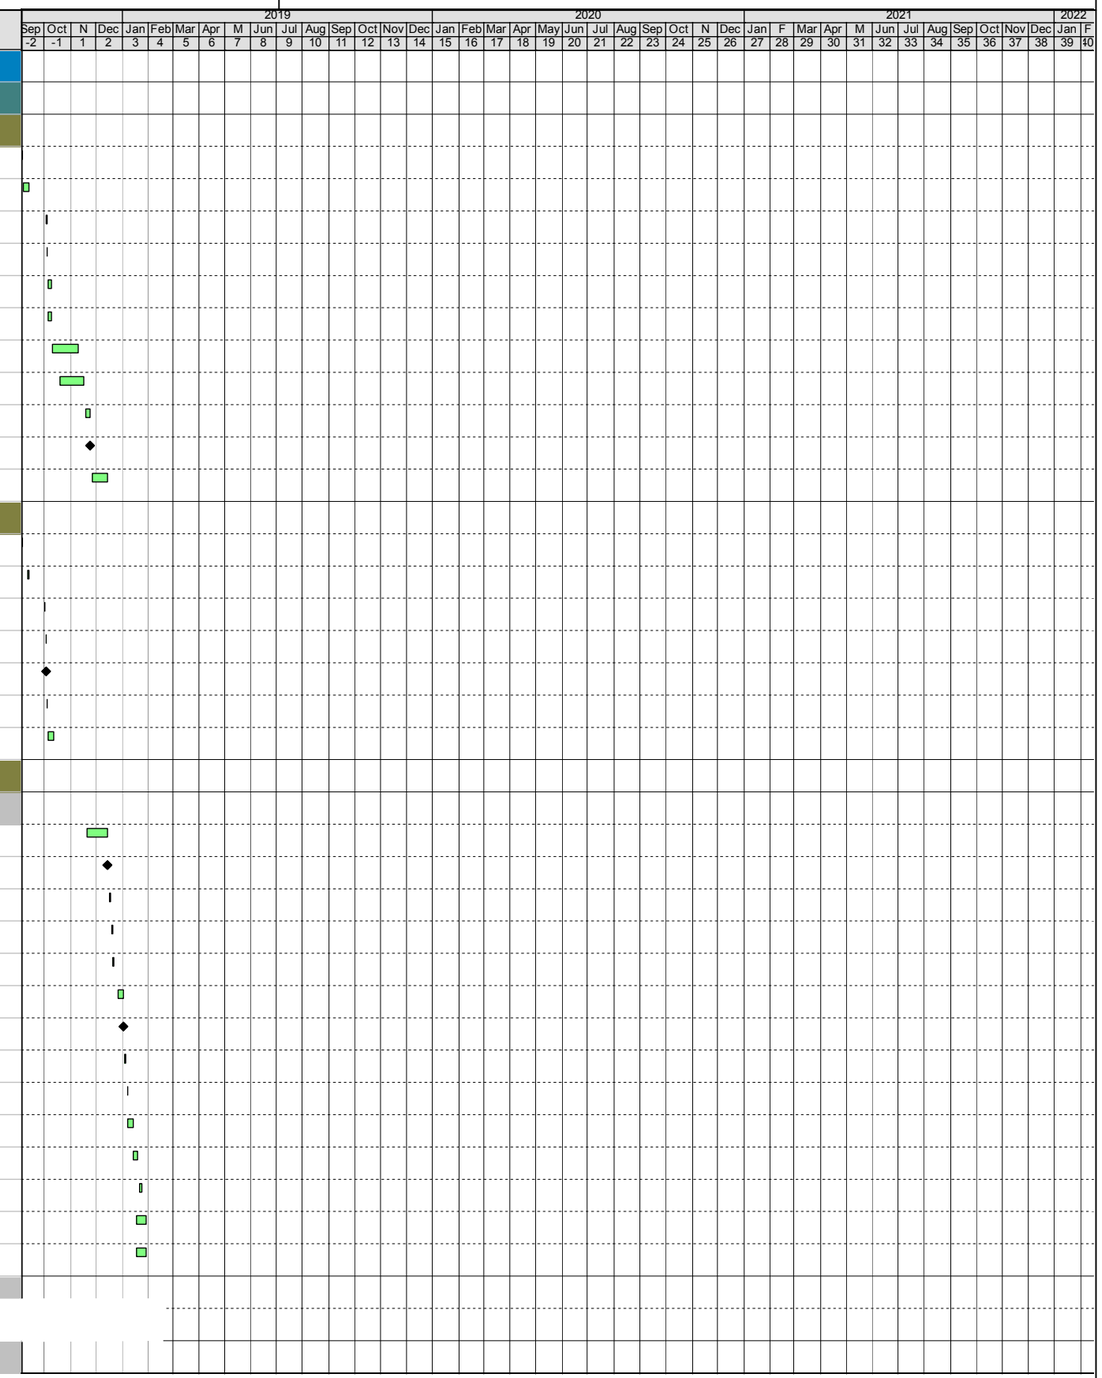

EllisDon
We build on great relationships™

Data Date :31-Aug-18 Run Date : 19-Oct-18
TASK filter: Submittal Schedule_1.

Royal Inland Hospital Patient Care Tower Project - Project Schedule

Date	Revision	Checked	Approved
19-Oct-18	Financial Close Schedule		

Activity ID	Activity Name	Original Duration	Start	Finish
DD-460	Arch background Freeze for DD #2	15	24-Jan-19	14-Feb-19
DD-465	MEIT Co-ordination & Production	10	15-Feb-19	28-Feb-19
DD-470	ED Receives DD#2 Pkg for QA/QC (Including MEP Info)	0		28-Feb-19
DD-480	QA/QC Review by ED/Trades/FM & QA/QC Mark up issued for Consultant	3	01-Mar-19	05-Mar-19
DD-490	Consultant prepare Revised Pkg & Issue to ED	5	06-Mar-19	12-Mar-19
DD-500	ED/Trades/FM QA/QC # 2	2	13-Mar-19	14-Mar-19
DD-505	Consultant prepare Revised Pkg & Issue to ED	1	15-Mar-19	15-Mar-19
DD-510	Issue to Printer	0		15-Mar-19
DD-520	Print Dwg	2	16-Mar-19	17-Mar-19
DD-530	Draft Pkg Delivered to IH #2	1	18-Mar-19	18-Mar-19
DD-540	Wait Time between Submission and UCGs	7	19-Mar-19	25-Mar-19
DD-550	Clinical : User Consultation Meeting	5	26-Mar-19	01-Apr-19
DD-560	Technical : User Consultation Meeting	3	02-Apr-19	04-Apr-19
DD-570	Project to Circulate Live Minutes	8	29-Mar-19	09-Apr-19
DD-580	Informal Feedback from the Authority	8	29-Mar-19	09-Apr-19
DD - IMIT		60	20-Nov-18	21-Feb-19
A3130	Preliminary Layouts - Eqmnt Racks in MCC, Demark & TR's	30	20-Nov-18	09-Jan-19
A3140	Preliminary Layouts - WAP / RTLS / Security / Nurse Call / AV Design	30	10-Jan-19	21-Feb-19
DD#3		71	05-Apr-19	18-Jul-19
DD-590	Arch background Freeze for DD #3	5	05-Apr-19	11-Apr-19
DD-595	MEIT Co-ordination & Production	10	12-Apr-19	29-Apr-19
DD-600	ED Receives DD#3 Pkg for QA/QC (Including MEP Info)	0		29-Apr-19
DD-610	QA/QC Review by ED/Trades/FM & QA/QC Mark up issued for Consultant	3	30-Apr-19	02-May-19
DD-620	Consultant prepare Revised Pkg & Issue to ED	5	03-May-19	09-May-19
DD-630	ED/Trades/FM QA/QC # 2	2	10-May-19	13-May-19
DD-635	Consultant prepare Revised Pkg & Issue to ED	1	14-May-19	14-May-19
DD-640	Issue to Printer	0		14-May-19
DD-650	Print Dwg	2	15-May-19	16-May-19
DD-660	Draft Pkg Delivered to IH #3	1	17-May-19	17-May-19
DD-670	Wait Time between Submission and UCGs	7	18-May-19	24-May-19
DD-680	Clinical : User Consultation Meeting	5	27-May-19	31-May-19
DD-690	Technical : User Consultation Meeting	3	03-Jun-19	05-Jun-19
DD-700	Project to Circulate Live Minutes	8	30-May-19	10-Jun-19
DD-710	Informal Feedback from the Authority	8	30-May-19	10-Jun-19
DD-715	Project Co., Prepare & Submit for Formal Design Development Submittal	0		26-Jun-19
DD-718	Authority Review Timeline for Formal Design Development	15	27-Jun-19	18-Jul-19
Construction Documents Breakout Packages		459	20-Aug-18 A	17-Jul-20
Early Works (Site Utility Relocation)		36	20-Aug-18 A	23-Oct-18
CD-1840	Prepare 95% CD	25	20-Aug-18 A	11-Sep-18
CD-1850	Submit for IH Authority Approval	0		11-Sep-18
CD-1860	Authority Review and Comments	15	11-Sep-18	01-Oct-18

Data Date :31-Aug-18 Run Date : 19-Oct-18
TASK filter: Submittal Schedule_1.

Royal Inland Hospital Patient Care Tower Project - Project Schedule

Date	Revision	Checked	Approved
19-Oct-18	Financial Close Schedule		

Activity ID	Activity Name	Original Duration	Start	Finish
CD-1870	Prepare and Issue IFCs	15	02-Oct-18	23-Oct-18
Bulk Excavation		30	25-Sep-18	07-Nov-18
CD-1810	Submit for IH Authority Approval	0		25-Sep-18*
CD-1820	Authority Review and Comments	15	26-Sep-18	17-Oct-18
CD-1830	Prepare and Issue IFCs	15	18-Oct-18	07-Nov-18
Sleeving,Foundations / Substructure (to the u/s of 1st suspended slab)		101	11-Dec-18	14-May-19
CD-100	Prepare 50% CD	20	11-Dec-18	17-Jan-19
CD-110	ED Review/QA-QC	10	18-Jan-19	01-Feb-19
CD-115	50 CDs - Submit for Authority Review	0	01-Feb-19	01-Feb-19
CD-120	Prepare 95% CD	25	01-Feb-19	11-Mar-19
CD-130	Submit for IH Authority Approval	0		11-Mar-19
CD-140	Authority Review and Comments	15	11-Mar-19	29-Mar-19
CD-950	Prepare and Issue 100% CDs	15	01-Apr-19	23-Apr-19
CD-975	IH Approval of the 100 CDs	15	24-Apr-19	14-May-19
Elevators		55	01-Feb-19	23-Apr-19
CD-0980	Prepare for IH Elevator Pit Size	25	01-Feb-19	11-Mar-19
CD-0990	Submit for IH Authority Approval - Pit Size	0		11-Mar-19
CD-1000	Authority Review and Comments	15	11-Mar-19	29-Mar-19
CD-1010	Prepare and Issue IFCs	15	01-Apr-19	23-Apr-19
Sleeving,Blockouts and Superstructure (1st suspended slab thru Roof)		142	07-Feb-19	03-Sep-19
CD-1020	Prepare 50% CD	60	07-Feb-19	07-May-19
CD-1030	ED Review and issue comments	10	08-May-19	23-May-19
CD-1040	Prepare 95% CD	25	24-May-19	27-Jun-19
CD-1050	Submit for IH Authority Approval	0		27-Jun-19
CD-1060	Authority Review and Comments	15	28-Jun-19	19-Jul-19
CD-1070	Prepare and Issue 100% CDs	15	22-Jul-19	12-Aug-19
CD-1150	IH Approval of the 100 CDs	15	13-Aug-19	03-Sep-19
Doors / Hardware / Access control		159	19-Jul-19	16-Mar-20
A12550	50CDs- Prepare and Submit Door and Hardware Details	54	19-Jul-19	04-Oct-19
A12560	50CDs-IH Review & Approvals	15	07-Oct-19	28-Oct-19
A12570	95CDs-Prepare and Submit Door and Hardware Details	40	29-Oct-19	03-Jan-20
A12580	95CDs-IH Review and Approvals	15	06-Jan-20	24-Jan-20
A12590	Prepare 100CDs and Submit for IH Approval	20	27-Jan-20	24-Feb-20
A12600	100CDs - IH review and Approvals of Doors and Hardware	15	25-Feb-20	16-Mar-20
Major Mech Equipment		157	27-Mar-19	13-Nov-19
CD-1320	Prepare 50% CD	70	27-Mar-19	09-Jul-19
CD-1330	ED Review and issue comments	10	10-Jul-19	24-Jul-19
CD-1340	Prepare 95% CD	25	25-Jul-19	30-Aug-19
CD-1350	Submit for IH Authority Approval	0		30-Aug-19
CD-1360	Authority Review and Comments	15	30-Aug-19	23-Sep-19
CD-1890	Prepare 100% CDs & Submit to IH for Review	20	23-Sep-19	22-Oct-19

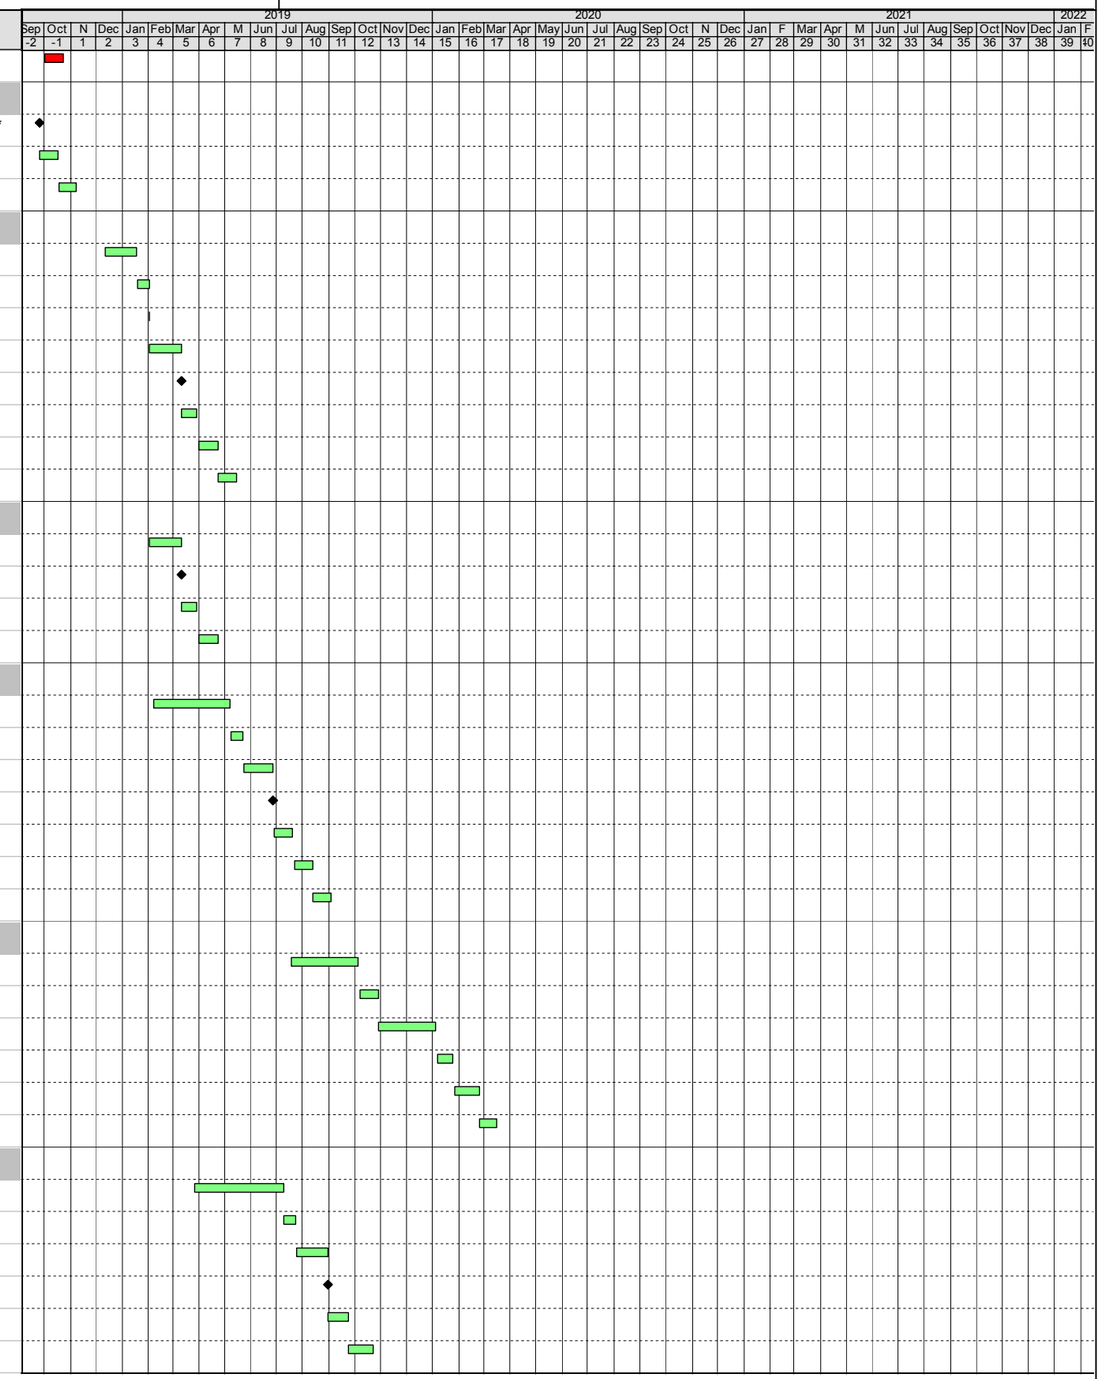

EllisDon
We build on great relationships™

Data Date :31-Aug-18 Run Date : 19-Oct-18
TASK filter: Submittal Schedule_1.

Royal Inland Hospital Patient Care Tower Project - Project Schedule

Date	Revision	Checked	Approved
19-Oct-18	Financial Close Schedule		

Activity ID	Activity Name	Original Duration	Start	Finish
CD-1900	IH Review	15	22-Oct-19	13-Nov-19
Major Elec Equipment		157	10-Jun-19	03-Feb-20
CD-1380	Prepare 50% CD & Submit to IH for Review	70	10-Jun-19	19-Sep-19
CD-1390	IH Review	10	20-Sep-19	04-Oct-19
CD-1400	Prepare 95% CD & Submit to IH for Review	25	07-Oct-19	13-Nov-19
CD-1410	Submit for IH Authority Approval	0		13-Nov-19
CD-1420	Authority Review and Comments	15	13-Nov-19	04-Dec-19
CD-1430	Prepare 100% CDs & Submit to IH for Review	20	04-Dec-19	13-Jan-20
CD-1880	IH Review	15	13-Jan-20	03-Feb-20
50% Construction Documents (IMIT)		35	19-Jul-19	09-Sep-19
CD-IC-100	Updated Equipment Layouts and elevations - MC, Demark & TR's	20	19-Jul-19	16-Aug-19
CD-IC-110	Updated Layouts of RTLS /AV / Digital Signages / Kiosk etc	20	19-Jul-19	16-Aug-19
CD-IC-120	Updated WAP Design & Wireless Coverage Simulation	20	19-Jul-19	16-Aug-19
CD-IC-130	Updated Layouts, end device count and rack elevations of MCC, Demark & TR's	20	19-Jul-19	16-Aug-19
CD-IC-140	Preliminary Network, Wireless, Telephony, RTLS, Servers & SAN Design	15	19-Aug-19	09-Sep-19
100% Construction Documents (IMIT)		60	29-Oct-19	31-Jan-20
A3100	Final layout of all IP dependeent systems such as RTLS, Nurse Call, Security etc	40	29-Oct-19	03-Jan-20
A3110	Finalize Design - Network Gear, Wireless, Telephony, RTLS, DAS, Server & SAN	20	06-Jan-20	31-Jan-20
A3120	Finalize Technical specifications for equipments	20	06-Jan-20	31-Jan-20
Envelope		157	02-Jul-19	24-Feb-20
CD-1080	Prepare 50% CD	70	02-Jul-19	10-Oct-19
CD-1090	IH Review	15	11-Oct-19	04-Nov-19
CD-1100	Prepare 95% CD	25	05-Nov-19	10-Dec-19
CD-1110	Submit for IH Authority Approval	0		10-Dec-19
CD-1120	Authority Review and Comments	15	11-Dec-19	10-Jan-20
CD-1130	Prepare 100% CDs & Submit to IH for Review	15	13-Jan-20	31-Jan-20
CD-1140	IH Review	15	03-Feb-20	24-Feb-20
[Parkade Thru Lvl 3]Studs/Partitions/OH Mech & Elec,Paint,HeadWalls,Pneumatic Tubes,Millwork,Signage		159	19-Jul-19	16-Mar-20
BD-1000	Prepare 50% CD & Submit to IH for Review	54	19-Jul-19	04-Oct-19
BD-1010	50% CD IH Review	15	07-Oct-19	28-Oct-19
BD-1020	Prepare 95% CD to IH for Review	40	29-Oct-19	03-Jan-20
BD-1030	Submit for IH Authority Approval	0		03-Jan-20
BD-1040	Authority Review and Comments	15	06-Jan-20	24-Jan-20
BD-1050	Prepare 100% CDs & Submit to IH for Review	20	27-Jan-20	24-Feb-20
BD-2070	IH Review	15	25-Feb-20	16-Mar-20
[Lvl 4 Thru Roof]Studs/Partitions/OH Mech & Elec,Paint,HeadWalls,Pneumatic Tubes,Millwork,Signage		229	19-Jul-19	25-Jun-20
BD-2000	Prepare 50% CD & Submit to IH for Review	54	19-Jul-19	04-Oct-19
BD-2010	50% CD IH Review	15	07-Oct-19	28-Oct-19
BD-2020	Prepare 95% CD & Submit to IH for Review	65	29-Oct-19	07-Feb-20
BD-2030	Submit for IH Authority Approval	0		07-Feb-20
BD-2040	Authority Review and Comments	15	11-Feb-20	02-Mar-20

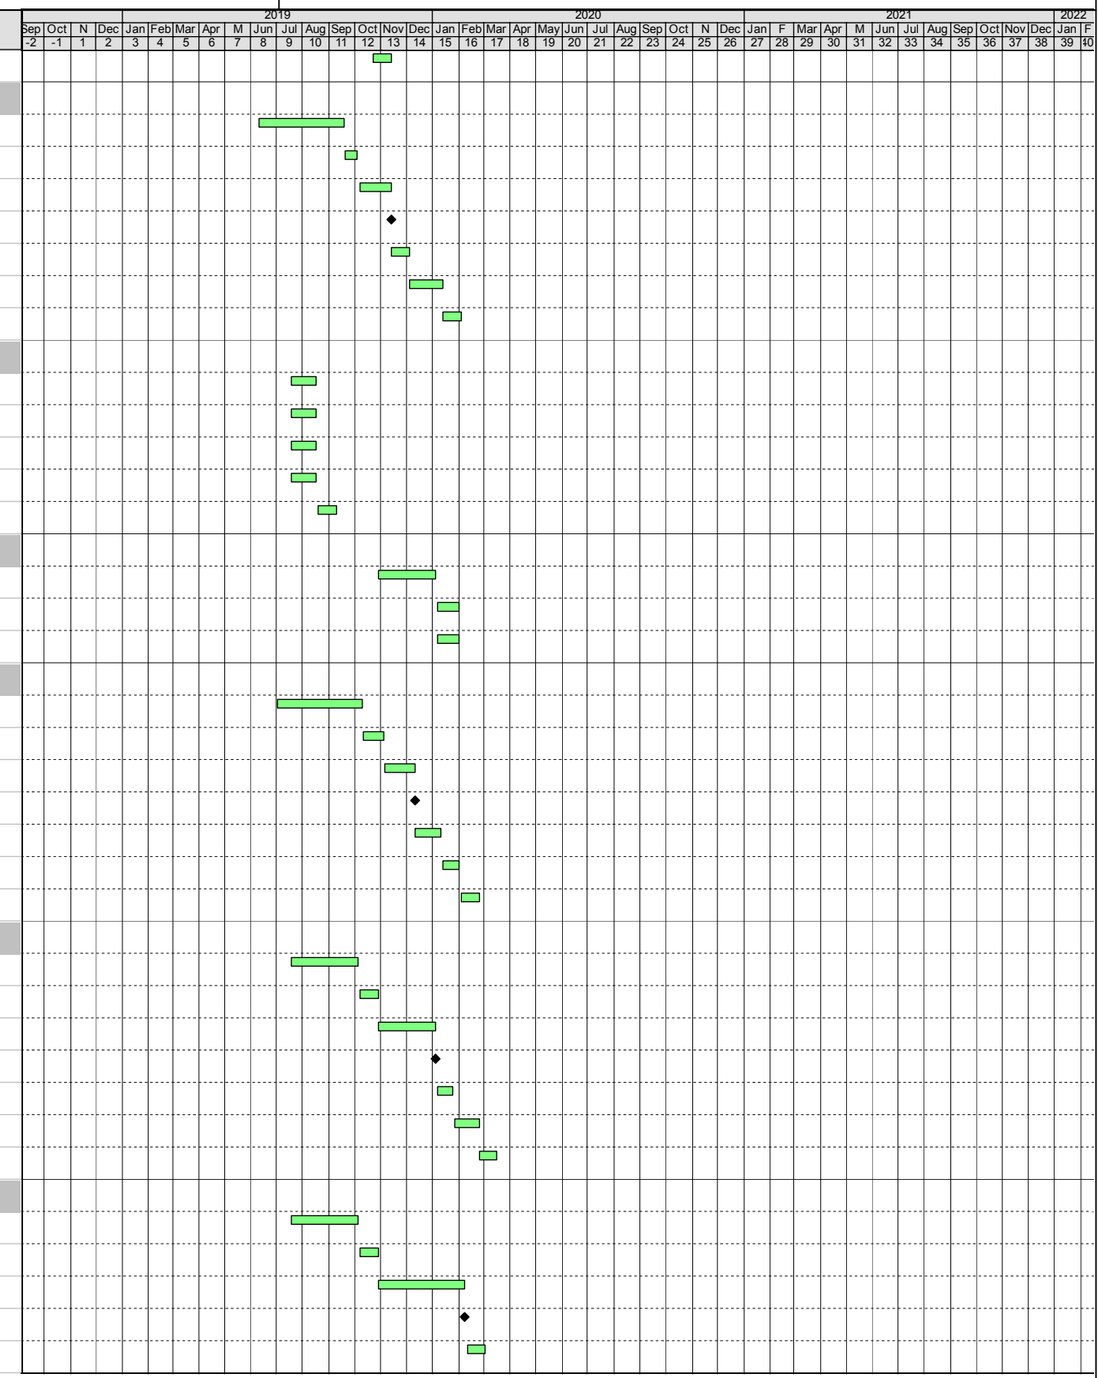

Data Date :31-Aug-18 Run Date : 19-Oct-18
TASK filter: Submittal Schedule_1.

Royal Inland Hospital Patient Care Tower Project - Project Schedule

Date	Revision	Checked	Approved
19-Oct-18	Financial Close Schedule		

Activity ID	Activity Name	Original Duration	Start	Finish
BD-2050	Prepare 100% CDs & Submit to IH for Review	65	03-Mar-20	04-Jun-20
BD-2060	IH Review	15	05-Jun-20	25-Jun-20
Shallow Civil utilities / landscaping / paving		82	20-Mar-20	17-Jul-20
CD-1560	Prepare 50% CD	15	20-Mar-20	14-Apr-20
CD-1570	ED Review and issue comments	10	15-Apr-20	29-Apr-20
CD-1580	Prepare 95% CD	25	30-Apr-20	05-Jun-20
CD-1590	Submit for IH Authority Approval	0		05-Jun-20
CD-1600	Authority Review and Comments	15	05-Jun-20	26-Jun-20
CD-1610	Prepare and Issue IFCs	15	26-Jun-20	17-Jul-20
50% Construction Documents		69	19-Jul-19	28-Oct-19
CD-50-100	Arch background Freeze for CD 50	30	19-Jul-19	30-Aug-19
CD-50-105	MEIT Co-ordination & Production	10	03-Sep-19	16-Sep-19
CD-50-110	ED Receives CD 50 Pkg for QA/QC (Including MEP Info)	0		16-Sep-19
CD-50-120	QA/QC Review by ED/Trades/FM & QA/QC Mark up issued for Consultant	3	17-Sep-19	19-Sep-19
CD-50-130	Consultant prepare Revised Pkg & Issue to ED	5	20-Sep-19	26-Sep-19
CD-50-140	ED/Trades/FM QA/QC # 2	2	27-Sep-19	30-Sep-19
CD-50-145	Consultant prepare Revised Pkg & Issue to ED	1	01-Oct-19	01-Oct-19
CD-50-150	Issue to Printer	0		01-Oct-19
CD-50-160	Print Dwg	2	02-Oct-19	03-Oct-19
CD-50-170	Formal CD 50 Pkg Delivered to IH	1	04-Oct-19	04-Oct-19
CD-50-240	Authority Review Timeline for Formal CD-50	15	07-Oct-19	28-Oct-19
95% Construction Documents		80	29-Oct-19	02-Mar-20
CD-95-100	Arch background Freeze for CD 95	40	29-Oct-19	03-Jan-20
CD-95-105	MEIT Co-ordination & Production	10	06-Jan-20	17-Jan-20
CD-95-110	ED Receives CD 95 Pkg for QA/QC (Including MEP Info)	0		17-Jan-20
CD-95-120	QA/QC Review by ED/Trades/FM & QA/QC Mark up issued for Consultant	3	20-Jan-20	22-Jan-20
CD-95-130	Consultant prepare Revised Pkg & Issue to ED	5	24-Jan-20	30-Jan-20
CD-95-140	ED/Trades/FM QA/QC # 2	2	31-Jan-20	03-Feb-20
CD-95-145	Consultant prepare Revised Pkg & Issue to ED	1	04-Feb-20	04-Feb-20
CD-95-150	Issue to Printer	0		04-Feb-20
CD-95-160	Print Dwg	2	05-Feb-20	06-Feb-20
CD-95-170	Formal CD 95 Pkg Delivered to IH	1	07-Feb-20	07-Feb-20
CD-95-240	Authority Review Timeline for Formal CD-95	15	11-Feb-20	02-Mar-20
100% Construction Documents		115	03-Mar-20	17-Aug-20
100-CD-110	Arch background Freeze for CD 100	40	03-Mar-20	29-Apr-20
100-CD-120	MEIT Co-ordination & Production	10	30-Apr-20	13-May-20
100-CD-130	ED Receives CD 100 Pkg for QA/QC (Including MEP Info)	0		13-May-20
100-CD-140	QA/QC Review by ED/Trades/FM & QA/QC Mark up issued for Consultant	3	14-May-20	19-May-20
100-CD-150	Consultant prepare Revised Pkg & Issue to ED	5	21-May-20	27-May-20
100-CD-160	ED/Trades/FM QA/QC # 2	2	28-May-20	29-May-20
100-CD-170	Consultant prepare Revised Pkg & Issue to ED	1	01-Jun-20	01-Jun-20

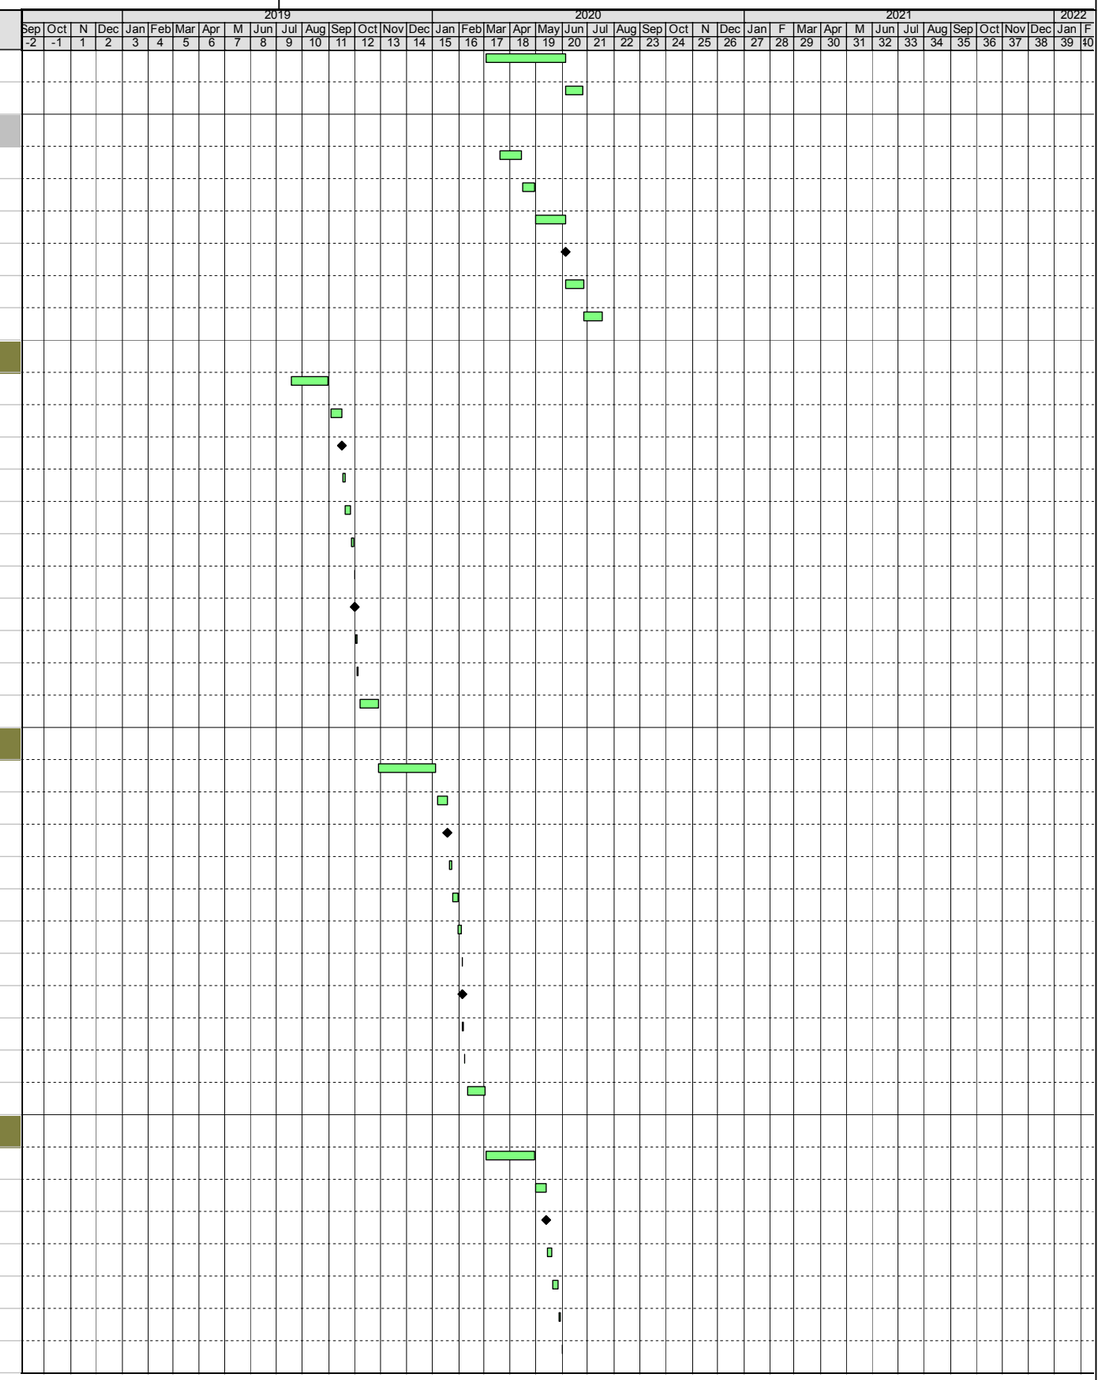

Data Date :31-Aug-18 Run Date : 19-Oct-18
TASK filter: Submittal Schedule_1.

Royal Inland Hospital Patient Care Tower Project - Project Schedule

Date	Revision	Checked	Approved
19-Oct-18	Financial Close Schedule		

Activity ID	Activity Name	Original Duration	Start	Finish
100-CD-180	Issue to Printer	0		01-Jun-20
100-CD-190	Print Dwg	2	02-Jun-20	03-Jun-20
100-CD-200	Formal CD 100 Delivered to IH	1	04-Jun-20	04-Jun-20
100-CD-210	Authority Review Timeline for 100% CDs	15	05-Jun-20	25-Jun-20*
100-CD-220	Revise the Dwg and incorporate Changes in 100% CDs R1	20	26-Jun-20	24-Jul-20
100-CD-230	Authority Review and Sign off	15	27-Jul-20	17-Aug-20
100 % IFCs		20	26-Jun-20	24-Jul-20
100IFC-100	Prepare and Complete 100% IFCs	20	26-Jun-20	24-Jul-20*
Mock Ups		521	21-Feb-19	07-Apr-21
Paper Mock Up (Sch 2 Sec 5.5(a)) (19 Rooms)		10	21-Feb-19	06-Mar-19
DD-M-120	Construction Paper Mock up - Further Review with Authority to Come	2	21-Feb-19	22-Feb-19
DD-M-130	Authority Review of the Paper Mock Up and Provide Feedback	5	25-Feb-19	01-Mar-19
DD-M-140	Project Co to issue Paper Mock-Up Minutes to Authority	3	04-Mar-19	06-Mar-19
Fully Constructed Mock Ups (Sch 2 Sec 5.5(b)) (17 Rooms)		146	15-Mar-19	15-Oct-19
DD-M-150	Prepare Mock Up Design for Authority Review	0		15-Mar-19*
DD-M-160	Authority Review Timeline for Approval of Mock Up	15	18-Mar-19	05-Apr-19
DD-M-165	Sub-Trade:Procurement and Delivery of Mock Up	60	15-Mar-19	11-Jun-19
DD-M-170	Construct Fully Constructed Mock Up	60	08-May-19	01-Aug-19
DD-M-175	Authority Informal User Walk Through to Compile Comment Log	9	01-Aug-19	14-Aug-19
DD-M-180	Authority Review of the Constructed Mock Up and Provide Feedback	7	15-Aug-19	23-Aug-19
DD-M-190	Correction to Fully Constructed Mock Up Drawings	19	26-Aug-19	20-Sep-19
DD-M-200	Print Drawings	1	23-Sep-19	23-Sep-19
DD-M-210	Fully Constructed Mock Up revised drawings issued to Authority	0	24-Sep-19	24-Sep-19
DD-M-220	Authority Review Timeline	15	24-Sep-19	15-Oct-19
In Situ Mock Ups		215	22-May-20	07-Apr-21
A3150	In-Situ Mock - During the Construction Phase	215	22-May-20	07-Apr-21
Submittal To Authority		619	15-Nov-18	31-May-21
Energy Incentive Program (App 8C Sec 2.2)		45	15-Nov-18	28-Jan-19
A2690	Prepare and Submit Energy Studies and Building Energy Model to City & Authority (Within 30B Days of Financial Close)	30	15-Nov-18	07-Jan-19
A2700	Review and Approval	15	07-Jan-19	28-Jan-19
Quality Assurance Plan Sch 2 Sec 8.5		111	15-Nov-18	03-May-19
A2930	Submit Quality Assurance (Draft) To Authority (Within 90B Days of Financial Close)	90	15-Nov-18	13-Feb-19
A2940	Authority to Review andf Provide Comments	20	13-Feb-19	13-Mar-19
A2950	Project Prepare and Submit Revised Draft QAP	20	13-Mar-19	10-Apr-19
A2960	Authority Review and Approval of the Plan	15	10-Apr-19	03-May-19
Phasing Plan Sch 2 Sec 6.9(a)		36	15-Nov-18	15-Jan-19
L3-1340	Submit Phasing Plan Authority (Within 30B Days of Financial Close)	30	15-Nov-18	15-Dec-18
L3-1350	Authority to Review and Approval of the Plan	15	17-Dec-18	15-Jan-19
Waste Management Plan		36	15-Nov-18	15-Jan-19
L3-1360	Submit Waste Management Plan Authority (Within 30B Days of Financial Close)	30	15-Nov-18	15-Dec-18

Data Date :31-Aug-18 Run Date : 19-Oct-18
TASK filter: Submittal Schedule_1.

Royal Inland Hospital Patient Care Tower Project - Project Schedule

Date	Revision	Checked	Approved
19-Oct-18	Financial Close Schedule		
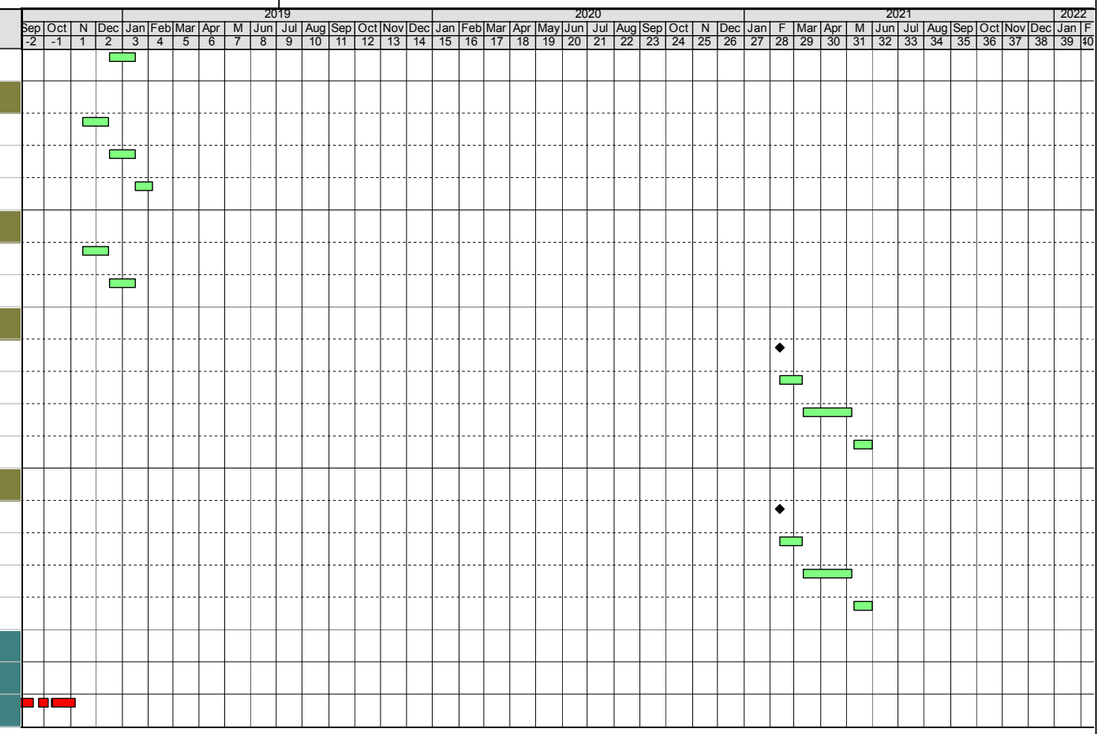
Activity ID	Activity Name	Original Duration	Start	Finish
L3-1370	Authority to Review and Approval of the Plan	15	17-Dec-18	15-Jan-19
Facility Threat and Risk Assessment		51	15-Nov-18	05-Feb-19
A2970	Prepare Facility Threat and Risk Assessment (Within 30B Days of Financial Close)	30	15-Nov-18	15-Dec-18
A2980	Authority Review and Approval	15	17-Dec-18	15-Jan-19
A2990	Project Co., to Prepare Final Report of the Facility and Risk Assessment	15	16-Jan-19	05-Feb-19
Demolition Plan		36	15-Nov-18	15-Jan-19
L3-1380	Submit Demolition Plan Authority (Within 30B Days of Financial Close)	30	15-Nov-18	15-Dec-18
L3-1390	Authority to Review and Approval of the Plan	15	17-Dec-18	15-Jan-19
Commissioning Plan		75	11-Feb-21	31-May-21
A3000	Submit Preliminary Draft Cx Plan (One Year Prior to Service Commencement)	0		11-Feb-21
A3010	Authority to Provide Comments	20	11-Feb-21	10-Mar-21
A3020	Project Co., to Prepare and Submit revised draft Cx Plan	40	11-Mar-21	07-May-21
A3030	Authority to review and Approve the Commissioning Plan	15	10-May-21	31-May-21
Move Plan		75	11-Feb-21	31-May-21
A3060	Submit Preliminary Draft Move Plan (One Year Prior to Service Commencement)	0		11-Feb-21
A3070	Authority to Provide Comments	20	11-Feb-21	10-Mar-21
A3080	Project Co., to Prepare and Submit revised Move Plan	40	11-Mar-21	07-May-21
A3090	Authority to review and Approve the Move Plan	15	10-May-21	31-May-21
Tendering and Award of Sub-Trades		379	31-Aug-18	23-Mar-20
Development Permit		82	19-Nov-18	22-Mar-19
Building Permits		344	03-Jul-18 A	31-Jan-20
